

Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

## MONTHLY REPORT

September 2020



**HAROLD MARTIN**  
SCHOOL



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

**MONTHLY REPORT INDEX**

September 2020

- |            |                          |
|------------|--------------------------|
| EXHIBIT 1: | CRITICAL ISSUES REPORT   |
| EXHIBIT 2: | PROJECT GMP REPORT       |
| EXHIBIT 3: | PROJECT SCHEDULE REPORT  |
| EXHIBIT 4: | FINANCIAL CHANGE SUMMARY |
| EXHIBIT 5: | PROJECT ALLOWANCE REPORT |
| EXHIBIT 6: | PROJECT PHOTOGRAPHY      |

Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

EXHIBIT 1

**CRITICAL ISSUES REPORT**

September 2020



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

## EXHIBIT 1

### CRITICAL ISSUES REPORT

September 2020

- Items impacting cost and schedule
  - Change Order for ERV at Preschool
  - FM System
  - Building Keying
  - Sprinkler System
- Items critical to schedule and remain under consideration:
  - Alternates
    - Alt #01 Nurses Suite \$146,070
    - Alt #02 Carpet Flooring Replacement at Classrooms \$86,514
    - Alt #03 Stair Flooring Replacement \$37,530
    - Alt #04 Construction Rooms 242,242,244, & 245 \$216,323
    - Alt #05 Additional Parking Spaces \$39,864
    - Alt #07 Northeast Roof Replacement \$82,251
    - Alt #08 Restroom Renovation \$125,995
- Risk & Concerns:
  - Schedule maintenance
  - Allowances
    - Winter Conditions
    - Temporary Heat

Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

MONTHLY REPORT  
EXHIBIT 2

**PROJECT GMP REPORT**

September 2020




### Contract Status Report - Thru September 2020

<b>Base Contract Value</b>				\$	<b>4,904,104.00</b>
<b>Contract Change Orders</b>				\$	<u>-</u>
<b>Total Contract Value</b>				\$	<b>4,904,104.00</b> <sup>1</sup>
<b>Contingency</b>					
	CM Contingency	\$	160,000.00		
<b>Estimated Cost to Complete</b>				\$	<b>4,521,753.27</b> <sup>2</sup>
<b>Retainage Held</b>				\$	<b>34,759.17</b> <sup>3</sup>

**Notes:**

- (1) from requisition 7 (G702)
- (2) from requisition 7 (G703 and General conditions report)
- (3) from requisition 7 (G702)

### Spend Out - Harold Martin School

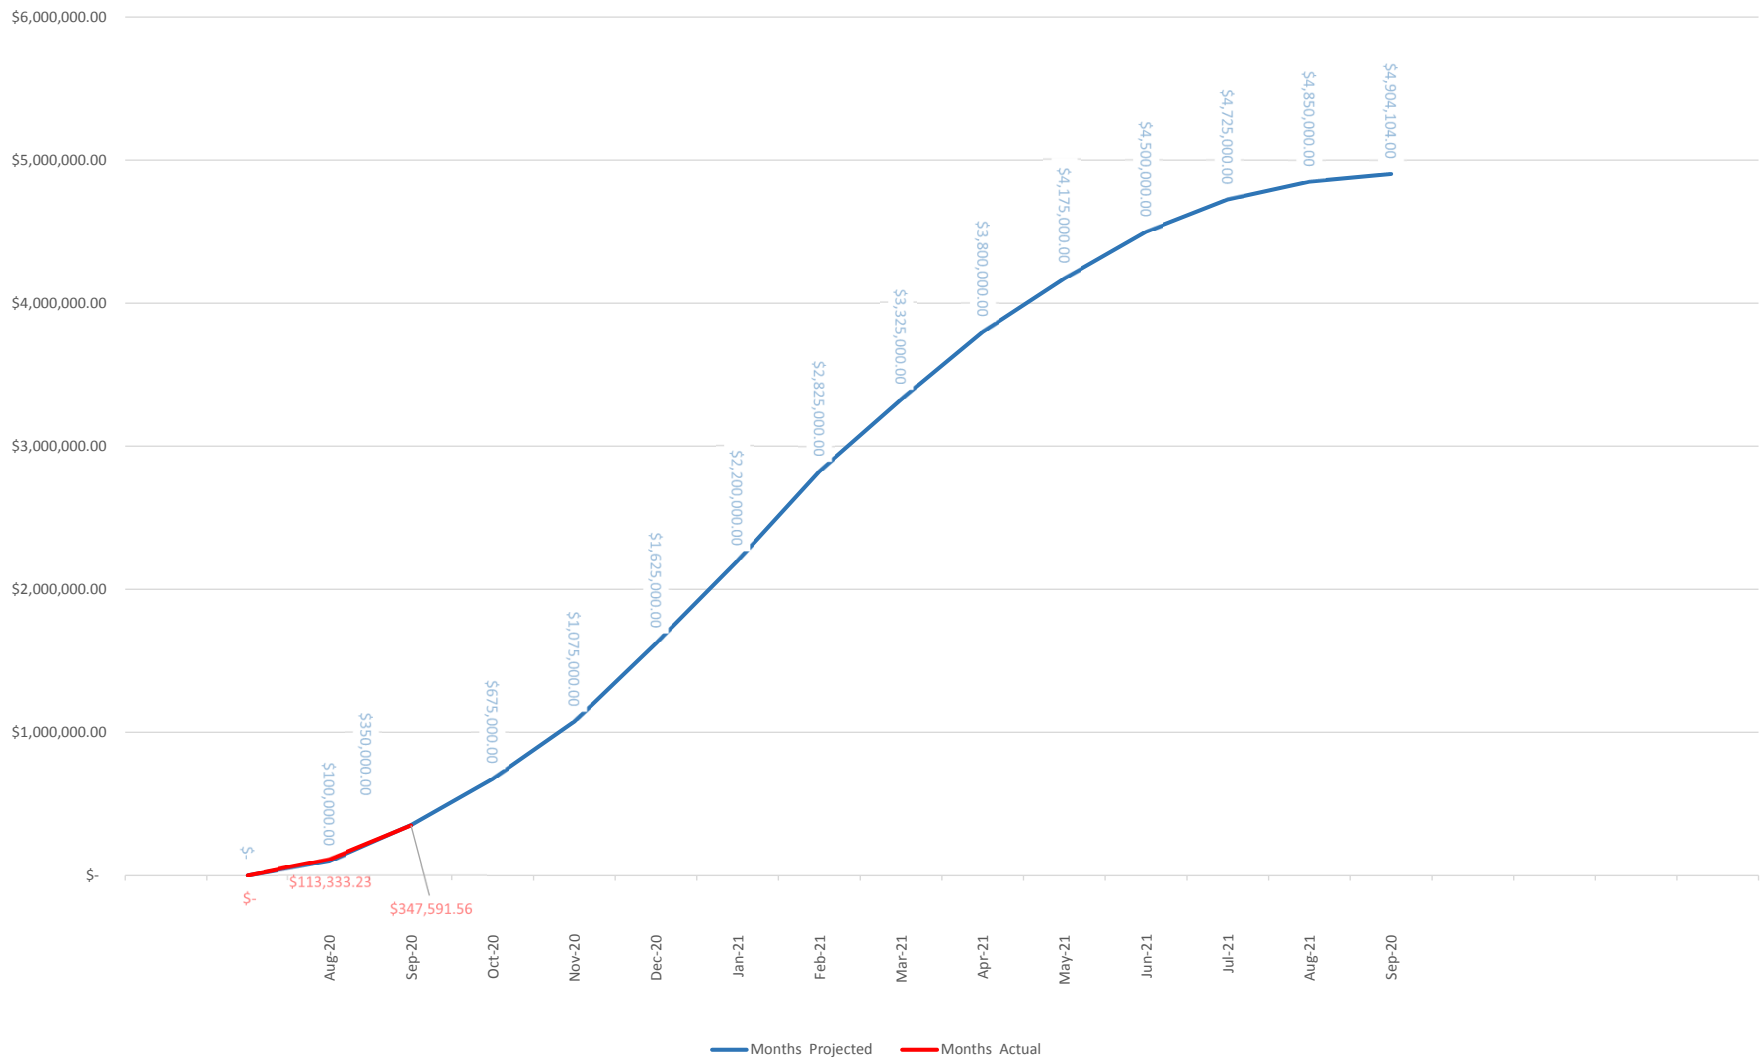



Harold Martin School  
Hopinton, New Hampshire

## GENERAL CONDITIONS REPORT

REQUISITION #02 - Dated: September 1, 2020 - September 30, 2020

### GENERAL CONDITIONS

		PREVIOUS APPLICATIONS	WORK IN PLACE	STORED MATERIALS	COMPLETED TO DATE	RETAINAGE
1	01-101 - Superintendent	\$ 6,766.50	\$ 10,023.00		\$ 16,789.50	\$ 1,678.95
2	01-102 - Time/Project Management	\$ 2,300.00	\$ 2,534.00		\$ 4,834.00	\$ 483.40
3	01-103 - Emg & Batters	\$ -	\$ -		\$ -	\$ -
4	01-105 - Temp Water	\$ -	\$ -		\$ -	\$ -
5	01-106 - Temp Barricades	\$ 5,789.35	\$ 1,689.38		\$ 7,478.73	\$ 747.87
6	01-107 - Temp Building	\$ 44.99	\$ 1,796.44		\$ 1,841.43	\$ 184.14
7	01-108 - Waste Management/Recycle	\$ -	\$ 3,534.00		\$ 3,534.00	\$ 353.40
8	01-109 - Communication/IT	\$ 659.60	\$ 738.05		\$ 1,397.65	\$ 139.77
9	01-110 - Small Tools	\$ -	\$ -		\$ -	\$ -
10	01-111 - Rental	\$ 250.00	\$ 4,468.83		\$ 4,718.83	\$ 471.88
11	01-113 - Temporary Toilet Facilities	\$ 1,543.40	\$ 587.97		\$ 2,131.37	\$ 213.14
12	01-114 - Temporary Power	\$ 499.95	\$ -		\$ 499.95	\$ 50.00
13	01-118 - Vehicles/Transportation	\$ 3,143.25	\$ 3,070.50		\$ 6,213.75	\$ 621.38
14	01-123 - Project Ads,Photos&Plans	\$ -	\$ -		\$ -	\$ -
15	01-124 - As Builts	\$ -	\$ -		\$ -	\$ -
16	01-128 - Bonds	\$ 25,528.00	\$ -		\$ 25,528.00	\$ 2,552.80
17	01-130 - Safety/OSHA Compliance	\$ 6,682.14	\$ 402.97		\$ 7,085.11	\$ 708.51
18	01-133 General Superintendent	\$ 960.00	\$ 1,600.00		\$ 2,560.00	\$ 256.00

<b>SUBTOTAL</b>	<b>\$ 54,167.18</b>	<b>\$ 30,445.14</b>	<b>\$ -</b>	<b>\$ 82,052.32</b>	<b>\$ 8,205.23</b>
-----------------	---------------------	---------------------	-------------	---------------------	--------------------





Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

MONTHLY REPORT  
EXHIBIT 3

**PROJECT SCHEDULE REPORT**

September 2020

# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
1	<b>Harold Martin School - Addition and Renovations</b>	<b>291 days</b>	<b>Harold Martin School - Addition and Renovations</b>											
2	<b>Construction Schedule</b>	<b>291 days</b>	<b>4% Construction Schedule</b>											
3	<b>Submittal Schedule</b>	<b>215 days</b>	<b>4% Submittal Schedule</b>											
43	<b>Renovations Work - Summer 2020</b>	<b>25 days</b>	<b>0% Renovations Work - Summer 2020</b>											
44	Roofing	25 days	<b>0% Roofing Eastern Exterior</b>											
45	<b>Renovations Work - Summer 2021</b>	<b>56 days</b>	<b>0% Renovations Work - Summer 2021</b>											
46	Demolition Restrooms and Nurses Suite	10 days	<b>0% Demolition Restrooms and Nurses Suite</b>											
47	Rough Restrooms & Nurses Suite	12 days	<b>0% Rough Restrooms &amp; Nurses Suite</b>											
48	Interior Wall Construction	10 days	<b>0% Interior Wall Construction</b>											
49	Electrical and Fire Alarm Rough Restrooms & Nurses Suite	12 days	<b>0% Electrical and Fire Alarm Rough Restrooms &amp; Nurses Suite</b>											
50	Mechanical Rough Restrooms & Nurses Suite	10 days	<b>0% Mechanical Rough Restrooms &amp; Nurses Suite</b>											
51	Install Blocking and repair walls restrooms & Nurses Suite	10 days	<b>0% Install Blocking and repair walls restrooms &amp; Nurses Suite</b>											
52	New Door Frames Restrooms & Nurses Suite	10 days	<b>0% New Door Frames Restrooms &amp; Nurses Suite</b>											
53	Painting Prime & First Coat Restrooms & Nurses Suite	10 days	<b>0% Painting Prime &amp; First Coat Restrooms &amp; Nurses Suite</b>											
54	Floor and Wall Tile Restrooms	7 days	<b>0% Floor and Wall Tile Restrooms</b>											
55	Floor Nurses Suite Flooring	2 days	<b>0% Floor Nurses Suite Flooring</b>											

Project: Harold Martin School Date: Fri 10/30/20	<table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 33%;">Task</td> <td style="width: 33%;"></td> <td style="width: 33%;">Inactive Summary</td> <td style="width: 33%;"></td> <td style="width: 33%;">External Tasks</td> </tr> <tr> <td>Split</td> <td></td> <td>Manual Task</td> <td></td> <td>External Milestone</td> </tr> <tr> <td>Milestone</td> <td></td> <td>Duration-only</td> <td></td> <td>Deadline</td> </tr> <tr> <td>Summary</td> <td></td> <td>Manual Summary Rollup</td> <td></td> <td>Critical</td> </tr> <tr> <td>Project Summary</td> <td></td> <td>Manual Summary</td> <td></td> <td>Critical Split</td> </tr> <tr> <td>Inactive Task</td> <td></td> <td>Start-only</td> <td></td> <td>Progress</td> </tr> <tr> <td>Inactive Milestone</td> <td></td> <td>Finish-only</td> <td></td> <td>Manual Progress</td> </tr> </table>	Task		Inactive Summary		External Tasks	Split		Manual Task		External Milestone	Milestone		Duration-only		Deadline	Summary		Manual Summary Rollup		Critical	Project Summary		Manual Summary		Critical Split	Inactive Task		Start-only		Progress	Inactive Milestone		Finish-only		Manual Progress
Task		Inactive Summary		External Tasks																																
Split		Manual Task		External Milestone																																
Milestone		Duration-only		Deadline																																
Summary		Manual Summary Rollup		Critical																																
Project Summary		Manual Summary		Critical Split																																
Inactive Task		Start-only		Progress																																
Inactive Milestone		Finish-only		Manual Progress																																

# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
56	ACT Ceiling Grid and Cuts Restrooms & Nurses Suite	7 days												
57	Install Fixtures Restrooms & Nurses Suite	7 days												
58	Install Toilet Partitions Restrooms	5 days												
59	Install Doors and Hardware Restrooms & Nurses Suite	5 days												
60	Finish Painting Restrooms & Nurses Suite	6 days												
61	Electrical and Mechanical Finishes Restrooms & Nurses Suite	6 days												
62	Install Toilet Accessories Restrooms	5 days												
63	Flood Ceiling Restrooms, Corridors & Nurses Suite	5 days												
64	Final Cleaning Restrooms & Nurses Suite	3 days												
65	<b>Summer Renovation Work Completed</b>	<b>0 days</b>												
66	<b>Addition 2018-2019</b>	<b>245 days</b>	<b>Addition 2018-2019</b>											
73	T&B for LP Line	3 days												
75	New Storm Drainage	3 days												
79	Structural Steel	10 days												
80	Install Joist & Metal Deck 2nd floor	10 days												
81	Install Joist & Metal Deck Roof	10 days												

Project: Harold Martin School Date: Fri 10/30/20	Task		Inactive Summary		External Tasks
	Split		Manual Task		External Milestone
	Milestone		Duration-only		Deadline
	Summary		Manual Summary Rollup		Critical
	Project Summary		Manual Summary		Critical Split
	Inactive Task		Start-only		Progress
	Inactive Milestone		Finish-only		Manual Progress

# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
82	<b>Structural Steel Complete</b>	<b>0 days</b>	<b>Structural Steel Complete</b> 											
83	Set Roof Curbs	5 days	<b>Set Roof Curbs</b> 											
84	Expansion Joint Materials	5 days	<b>Expansion Joint Materials</b> 											
85	1st Floor Cold Form Metal Framing	15 days	<b>1st Floor Cold Form Metal Framing</b> 											
86	1st Floor Blocking	5 days	<b>1st Floor Blocking</b> 											
87	1st Floor Gyp Drywall	10 days	<b>1st Floor Gyp Drywall</b> 											
88	<b>1st Floor weather tight</b>	<b>0 days</b>	<b>1st Floor weather tight</b> 											
89	2nd Floor Cold Form Metal Framing	15 days	<b>2nd Floor Cold Form Metal Framing</b> 											
90	2nd Floor Blocking	5 days	<b>2nd Floor Blocking</b> 											
91	2nd Floor Gyp Drywall	10 days	<b>2nd Floor Gyp Drywall</b> 											
92	<b>2nd Floor Weather Tight</b>	<b>0 days</b>	<b>2nd Floor Weather Tight</b> 											
93	Fire Wall	10 days	<b>Fire Wall</b> 											
94	Temp Heat	50 days	<b>Temp Heat</b> 											
95	Concrete Slab on Deck	5 days	<b>Concrete Slab on Deck</b> 											
96	Concrete Slab on Grade	5 days	<b>Concrete Slab on Grade</b> 											
97	Sprayfoam	30 days	<b>Sprayfoam</b> 											

Project: Harold Martin School Date: Fri 10/30/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress		

# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
98	Windows - 2nd Floor	10 days												
99	Windows - 1st Floor	10 days												
100	Brick Veneer	45 days												
101	Storefront/Entrance	15 days												
102	Insulated Metal Panels	10 days												
103	Curtain Wall	20 days												
104	Install Door Frames	20 days												
105	Light Gauge Metal Framing Interior Walls - 2nd floor	15 days												
106	Light Gauge Metal Framing Interior Walls - 1st Floor	15 days												
107	Insulation and Membrane Roofing	20 days												
108	Building Insulation - 2nd Floor	15 days												
109	Building Insulation - 1st Floor	15 days												
110	Under Slab Plumbing	15 days												
111	<b>Underslab Plumbing Complete</b>	<b>0 days</b>												
112	Mechanical Rough - 2nd Floor	30 days												
113	Mechanical Rough- 1st Floor	30 days												

Project: Harold Martin School Date: Fri 10/30/20	Task  Inactive Summary  External Tasks Split  Manual Task  External Milestone Milestone  Duration-only  Deadline Summary  Manual Summary Rollup  Critical Project Summary  Manual Summary  Critical Split Inactive Task  Start-only  Progress Inactive Milestone  Finish-only  Manual Progress
---	--

# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
114	Electrical Rough - 2nd Floor	30 days	<b>Electrical Rough - 2nd Floor</b>  0%											
115	Electrical Rough - 1st Floor	30 days	<b>Electrical Rough - 1st Floor</b>  0%											
116	Plumbing Rough - 2nd Floor	30 days	<b>Plumbing Rough - 2nd Floor</b>  0%											
117	Plumbing Rough - 1st Floor	30 days	<b>Plumbing Rough - 1st Floor</b>  0%											
118	Sprinkler Rough -2nd Floor	20 days	<b>Sprinkler Rough -2nd Floor</b>  0%											
119	Sprinkler Rough - 1st Floor	20 days	<b>Sprinkler Rough - 1st Floor</b>  0%											
120	<b>MEP Rough Complete</b>	<b>0 days</b>	<b>MEP Rough Complete</b>  0%											
121	Set Roof Top Units	5 days	<b>Set Roof Top Units</b>  0%											
122	Gypsum Drywall Hang - 2nd floor	20 days	<b>Gypsum Drywall Hang - 2nd floor</b>  0%											
123	Gypsum Drywall Hang - 1st Floor	20 days	<b>Gypsum Drywall Hang - 1st Floor</b>  0%											
124	Gypsum Drywall Tape & Sand - 2nd Floor	20 days	<b>Gypsum Drywall Tape &amp; Sand - 2nd Floor</b>  0%											
125	<b>2nd Floor Ready for Paint</b>	<b>0 days</b>	<b>2nd Floor Ready for Paint</b>  0%											
126	Gypsum Drywall Tape & Sand - 1st Floor	20 days	<b>Gypsum Drywall Tape &amp; Sand - 1st Floor</b>  0%											
127	<b>1st Floor Ready for Paint</b>	<b>0 days</b>	<b>1st Floor Ready for Paint</b>  0%											
128	Finish Carpentry / Architectural Millwork - 2nd Floor	20 days	<b>Finish Carpentry / Architectural Millwork - 2nd Floor</b>  0%											
129	Finish Carpentry / Architectural Millwork - 1st Floor	20 days	<b>Finish Carpentry / Architectural Millwork - 1st Floor</b>  0%											

Project: Harold Martin School Date: Fri 10/30/20	<table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 33%;">Task</td> <td style="width: 33%;"></td> <td style="width: 33%;">Inactive Summary</td> <td style="width: 33%;"></td> <td style="width: 33%;">External Tasks</td> </tr> <tr> <td>Split</td> <td></td> <td>Manual Task</td> <td></td> <td>External Milestone</td> </tr> <tr> <td>Milestone</td> <td></td> <td>Duration-only</td> <td></td> <td>Deadline</td> </tr> <tr> <td>Summary</td> <td></td> <td>Manual Summary Rollup</td> <td></td> <td>Critical</td> </tr> <tr> <td>Project Summary</td> <td></td> <td>Manual Summary</td> <td></td> <td>Critical Split</td> </tr> <tr> <td>Inactive Task</td> <td></td> <td>Start-only</td> <td></td> <td>Progress</td> </tr> <tr> <td>Inactive Milestone</td> <td></td> <td>Finish-only</td> <td></td> <td>Manual Progress</td> </tr> </table>	Task		Inactive Summary		External Tasks	Split		Manual Task		External Milestone	Milestone		Duration-only		Deadline	Summary		Manual Summary Rollup		Critical	Project Summary		Manual Summary		Critical Split	Inactive Task		Start-only		Progress	Inactive Milestone		Finish-only		Manual Progress
Task		Inactive Summary		External Tasks																																
Split		Manual Task		External Milestone																																
Milestone		Duration-only		Deadline																																
Summary		Manual Summary Rollup		Critical																																
Project Summary		Manual Summary		Critical Split																																
Inactive Task		Start-only		Progress																																
Inactive Milestone		Finish-only		Manual Progress																																


# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
130	Mechanical Finish - 2nd Floor	20 days												
131	Mechanical Finish -1st Floor	20 days												
132	Electrical Finish - 2nd Floor	20 days												
133	Electrical Finish - 1st Floor	20 days												
134	Plumbing Finish - 2nd Floor	15 days												
135	Toilet Partitios and Accessories - 2nd Floor	5 days												
136	Plumbing Finish - 1st Floor	15 days												
137	Toilet Partitios and Accessories - 1st Floor	5 days												
138	Sprinkler Finish - 2nd Floor	15 days												
139	Sprinkler Finish - 1st Floor	15 days												
140	Painting Prime and First Coat - 2nd Floor	15 days												
141	Install Lockers 2nd Floor	10 days												
142	Painting Prime and First Coat - 1st Floor	15 days												
143	ACT Ceiling - 2nd Floor	20 days												
144	ACT Ceiling - 1st Floor	20 days												
145	Flood Ceilings - 2nd Floor	10 days												

Project: Harold Martin School Date: Fri 10/30/20	Task		Inactive Summary		External Tasks
	Split		Manual Task		External Milestone
	Milestone		Duration-only		Deadline
	Summary		Manual Summary Rollup		Critical
	Project Summary		Manual Summary		Critical Split
	Inactive Task		Start-only		Progress
Inactive Milestone		Finish-only		Manual Progress	

# Harold Martin School

ID	Task Name	Duration	4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
			Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
146	Flood Ceilings - 1st Floor	10 days												
147	Flooring - 2nd Floor	15 days												
148	Flooring - 1st Floor	15 days												
149	Install Doors and Hardware - 2nd Floor	15 days												
150	Install Doors and Hardware - 1st Floor	15 days												
151	Final Painting - 2nd Floor	15 days												
152	Final Cleaning 2nd Floor	5 days												
153	Final Painting - 1st Floor	15 days												
154	Final Cleaning 1st Floor	5 days												
155	Mechanical Systems Balancing	10 days												
156	Punch List	20 days												
157	<b>Two Story Addition Completed</b>	<b>0 days</b>												
158	<b>Harold Martin School Complete</b>	<b>0 days</b>												



Project: Harold Martin School Date: Fri 10/30/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	



Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

MONTHLY REPORT  
EXHIBIT 4

**FINANCIAL CHANGE SUMMARY**

September 2020



Bonnette Page and Stone Corp.

Printed on Fri Oct 30, 2020 at 11:22 am EDT

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

## Change Events

Type : Owner Change

#	Title	Scope	Type	Reason	Status	Origin	ROM	Prime Totals	Commitment Totals	RFQs	Commitment COs	Prime PCOs
010	ERV Preschool Classroom	Out of Scope	Owner Change	Client request	Open		\$3,700.00	\$0.00	\$3,700.00		1	
009	DI Piping for Cistern	Out of Scope	Owner Change	Client request	Open		\$19,970.00	\$0.00	\$19,970.00		1	
005	Cistern for Fire Pump	Out of Scope	Owner Change	Client request	Open		\$83,384.88	\$0.00	\$81,550.00		2	
004	Horizontal Fire Pump & Tank Floats	Out of Scope	Owner Change	Client request	Open		\$44,785.50	\$0.00	\$43,800.00		1	
<b>Report Grand Totals</b>							<b>\$151,840.38</b>	<b>\$0.00</b>	<b>\$149,020.00</b>			



Bonnette Page and Stone Corp.

Printed on Fri Oct 30, 2020 at 11:20 am EDT

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

## Change Events

Type : Project Savings

#	Title	Scope	Type	Reason	Status	Origin	ROM	Prime Totals	Commitment Totals	RFQs	Commitment COs	Prime PCOs
002	Eliminate Wall Type E-1	Out of Scope	Project Savings	Client request	Closed		-\$19,800.00	\$0.00	-\$19,800.00		1	
001	Change from Cast Iron to PVC Pipe	Out of Scope	Project Savings	Client request	Closed		-\$17,000.00	\$0.00	-\$17,000.00		1	
<b>Report Grand Totals</b>							<b>-\$36,800.00</b>	<b>\$0.00</b>	<b>-\$36,800.00</b>			

Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

MONTHLY REPORT  
EXHIBIT 5

**PROJECT ALLOWANCES REPORT**

September 2020

Harold Martin School  
Hopkinton, NH



1-Sep-20

**Allowance Report**

	<b>Allowance Item</b>	<b>Amount</b>	<b>Actual</b>
1	Builders Risk Insurance	\$ 25,000.00	
2	Winter Weather	\$ 25,000.00	
3	Winter Heat	\$ 56,512.00	
4	CM Contigency	\$ 160,000.00	\$ 2,500.00
	Totals	\$ 266,512.00	\$ 2,500.00



Bonnette Page and Stone Corp.

Printed on Fri Oct 30, 2020 at 11:21 am EDT

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

## Change Events

Type : Contingency

#	Title	Scope	Type	Reason	Status	Origin	ROM	Prime Totals	Commitment Totals	RFQs	Commitment COs	Prime PCOs
008	RFI #04 - Moment Capacity & ASI #1 slab edge detail for winter conditions	Out of Scope	Contingency	Design development	Closed		\$2,500.00	\$0.00	\$2,500.00		1	
<b>Report Grand Totals</b>							<b>\$2,500.00</b>	<b>\$0.00</b>	<b>\$2,500.00</b>			

Phone: 603-524-3411

Fax: 603-524-4146

[www.bpsnh.com](http://www.bpsnh.com)



- A Better Building
- A Shorter Schedule
- A Substantial Savings

Hopkinton School District  
Harold Martin School  
271 Main Street  
Hopkinton, New Hampshire 03229

MONTHLY REPORT  
EXHIBIT 6

**PROJECT PHOTOGRAPHY**

September 2020



Bonnette Page and Stone Corp.

Printed on Fri Nov 13, 2020 at 07:32 am EST

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

plumbing

Description

Taken Date  
2020/09/28 11:30:43

Upload Date  
2020/09/28 13:31:17

Uploaded By  
Larry Brown

File Name  
[C8A8FC4F-9B1F-4306-A...](#)



plumbing


Description

Taken Date  
2020/09/28 11:30:38

Upload Date  
2020/09/28 11:30:49

Uploaded By  
Larry Brown

File Name  
[2653F3AE-39DA-4925-8...](#)

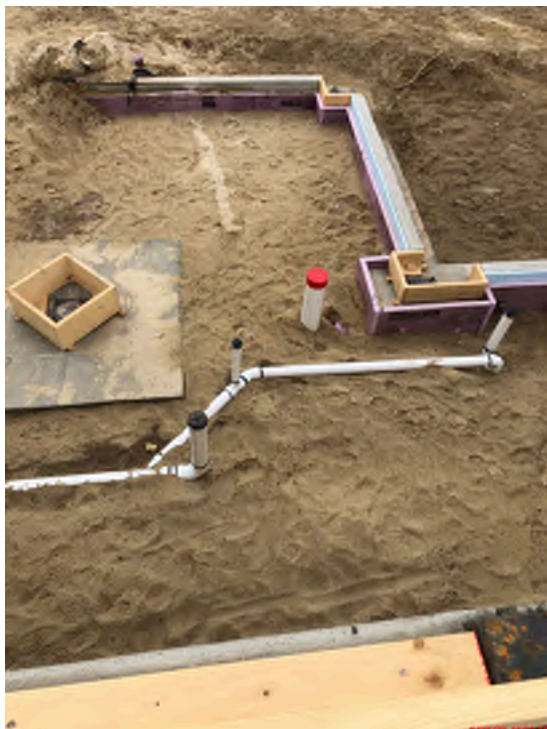





Bonnette Page and Stone Corp.

plumbing

Description

Taken Date  
2020/09/28 11:30:21

Upload Date  
2020/09/28 11:30:39

Uploaded By  
Larry Brown

File Name  
[B387617D-FA0C-4C99-A...](#)



plumbing

Description

Taken Date  
2020/09/28 11:30:12

Upload Date  
2020/09/28 11:30:29

Uploaded By  
Larry Brown

File Name  
[EE353531-D68F-419E-8...](#)





Bonnette Page and Stone Corp.

Printed on Fri Nov 13, 2020 at 07:32 am EST

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

insulation

Description

Taken Date  
2020/09/15 13:26:25

Upload Date  
2020/09/15 13:26:39

Uploaded By  
Larry Brown

File Name  
[26824C25-19B3-450A-B...](#)



insulation

Description

Taken Date  
2020/09/15 13:26:03

Upload Date  
2020/09/15 13:26:19

Uploaded By  
Larry Brown

File Name  
[D47BDECC-C42B-4A4C-...](#)





Bonnette Page and Stone Corp.

insulation

Description

Taken Date  
2020/09/15 08:32:32

Upload Date  
2020/09/15 08:32:45

Uploaded By  
Larry Brown

File Name  
[93CB1D9A-805B-46CE-A...](#)



insulation

Description

Taken Date  
2020/09/15 08:21:49

Upload Date  
2020/09/15 08:32:19

Uploaded By  
Larry Brown

File Name  
[053DE166-1B76-4F12-9...](#)





Bonnette Page and Stone Corp.

insulation

Description

Taken Date  
2020/09/15 08:21:44

Upload Date  
2020/09/15 08:22:09

Uploaded By  
Larry Brown

File Name  
[2F60C048-11BC-430A-B...](#)



foundation

Description

Taken Date  
2020/09/02 14:25:22

Upload Date  
2020/09/02 14:33:48

Uploaded By  
Larry Brown

File Name  
[35549C81-B3C0-4001-B...](#)





Bonnette Page and Stone Corp.

site

Description

Taken Date  
2020/09/01 14:30:38

Upload Date  
2020/09/01 16:22:13

Uploaded By  
Larry Brown

File Name  
[BA3D667B-1D8D-44E0-...](#)



foundation

Description

Taken Date  
2020/09/01 14:29:12

Upload Date  
2020/09/01 14:29:42

Uploaded By  
Larry Brown

File Name  
[C0A03240-6ED8-4BF1-B...](#)





Bonnette Page and Stone Corp.

Printed on Fri Nov 13, 2020 at 07:32 am EST

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

foundation

Description

Taken Date  
2020/09/01 14:29:03

Upload Date  
2020/09/01 14:29:27

Uploaded By  
Larry Brown

File Name  
[B4BED306-47F0-47F0-B...](#)



foundation

Description

Taken Date  
2020/09/01 14:29:00

Upload Date  
2020/09/01 14:29:15

Uploaded By  
Larry Brown

File Name  
[CD2FA0AA-5255-4674-9...](#)





Bonnette Page and Stone Corp.

Printed on Fri Nov 13, 2020 at 07:32 am EST

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

site

Description

Taken Date

Upload Date  
2020/09/01 11:19:47

Uploaded By  
Barrett Salta

File Name  
[hms3.jpg](#)



site

Description

Taken Date

Upload Date  
2020/09/01 11:19:46

Uploaded By  
Barrett Salta

File Name  
[hms2.jpg](#)





Bonnette Page and Stone Corp.

Printed on Fri Nov 13, 2020 at 07:32 am EST

749 HM Harold Martin School  
271 Main St  
Hopkinton, New Hampshire 03229

site

Description

Taken Date

Upload Date  
2020/09/01 11:19:46

Uploaded By  
Barrett Salta

File Name  
[hms1.jpg](#)

